



CIP Project Update


San Jacinto Plaza Reconstruction





San Jacinto Plaza

Site Plan

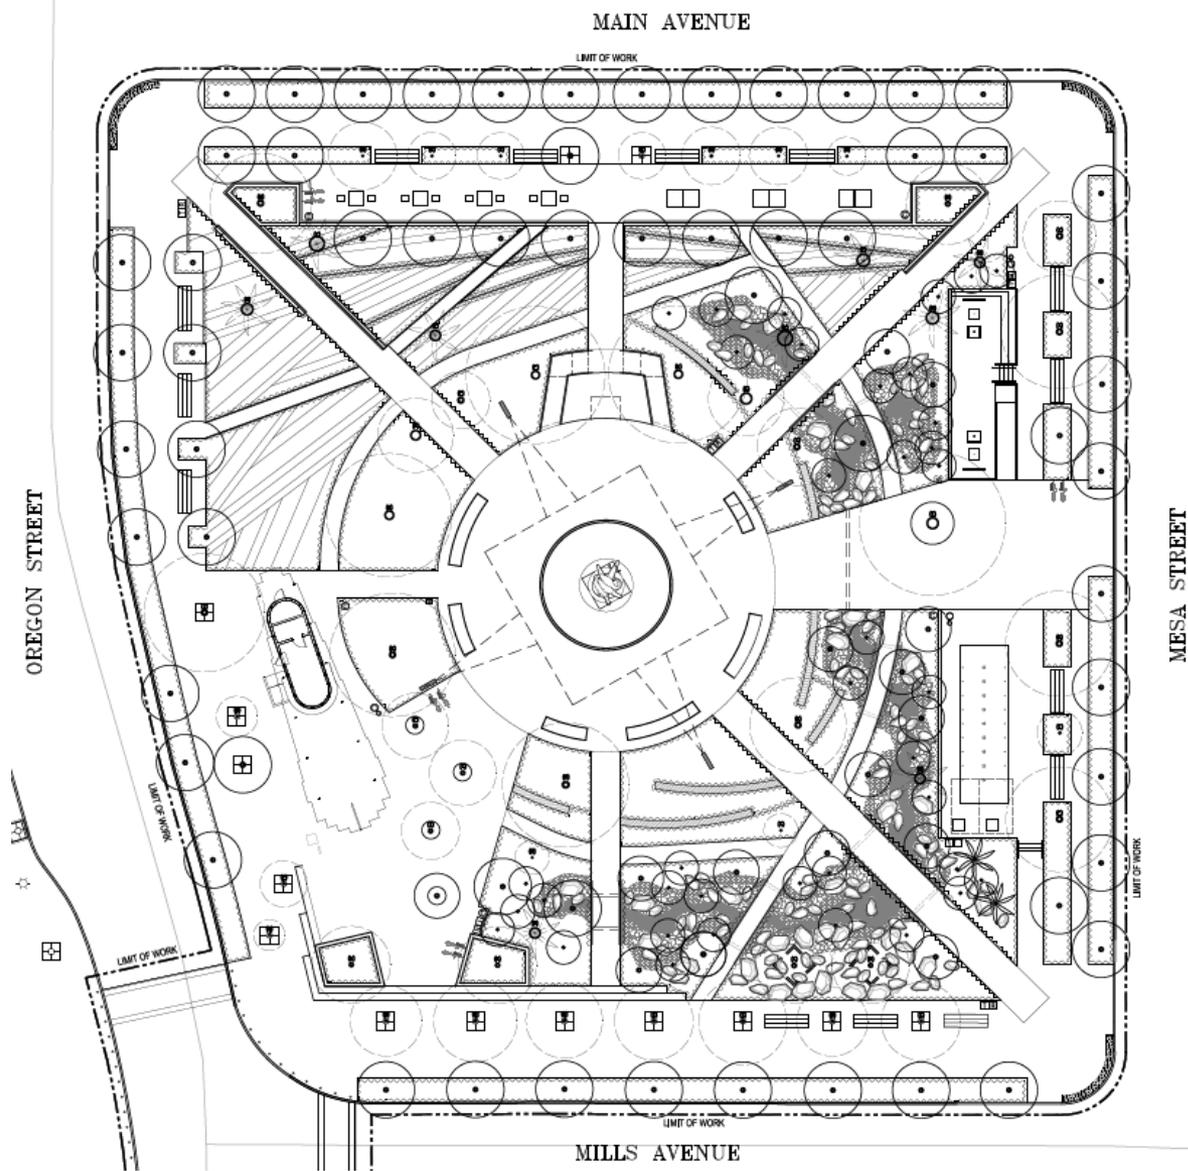



San Jacinto Plaza

Pedestrian Bridges





San Jacinto Plaza

Tree-lined Promenade – Main Street



San Jacinto Plaza

Landscaping Boulders





San Jacinto Plaza

Work In Progress

Project Element	Task Description	Status
Horseshoe / "Huacha" Court	Pit excavation and retaining walls	COMPLETE 
Landscaping	Underground irrigation system	In progress – 92%
	Underground electrical system	In progress – 92%
	Paver installation	In progress – 20%
	Installation of trees and shrubs	In progress
Splash pad water feature	Pad preparation/underground plumbing	In progress – 40%
	Splash pad vault	In progress – 85%
	Scheduled completion	Jan 29 2015



San Jacinto Plaza

Work In Progress

Project Element	Task Description	Status
Pedestrian Bridges	Form and pour concrete buttresses	COMPLETE 
	Steel beam fabrication	COMPLETE 
	Scheduled completion	Jan 9 2015
Café building	Steel framing	COMPLETE 
	Café electrical system	COMPLETE 
	Café canopy installation	In progress
	Final plumbing and mechanical	Jan 14 2015
	Scheduled completion	Jan 29 2015



San Jacinto Plaza

Work In Progress

Project Element	Task Description	Status
Sculpture Shade Canopy	Column installation	In progress – 30%
	Canopy fabrication	In progress – 20%
	Contract due date	Jan 29 2015
Site lighting	Delivery of lighting fixtures	Begun Nov 2014
	Scheduled completion	Jan 29 2015



San Jacinto Plaza

Threats to Project Completion

- **Structural shade canopy**
 - Contractor and Design Consultant coordinating efforts to expedite construction of shade canopy



San Jacinto Plaza

Approved Change Orders

Change Order No.	Description	Amount
1	Place traffic striping around San Jacinto Plaza to maintain public safety during construction	\$7,817.65
2	Remove and dispose of concrete subgrade material encountered along Mesa Street	\$25,555.56
3	Purchase and installation of additional mosaic tile incorrectly estimated	\$12,979.59
	Total	\$46,352.80



San Jacinto Plaza

Upcoming project modifications

Proposal	Description	Approximate cost
A	Purchase and installation of restroom facilities	\$400,000
B	Remove palm trees and replace with alternate tree species	\$60,000
C	Trim Plaza Christmas tree	Pending
D	Drinking fountain sewer connections	\$10,000
E	Relocate Christmas tree electrical controls to underground vault	\$20,000
F	Modify curb and gutter at Mills and Oregon to account for speed table deletion and storm drain installation	Pending



San Jacinto Plaza

Final Completion Date: February 28, 2015

CONSTRUCTION TIMELINE

0%

February 2014

70%

100%

February 2015



San Jacinto Plaza

Project Management Team

City of El Paso Project Manager	Rick Venegas Engineering and Construction Management
Contractor Project Manager	Eddie Linss Basic IDIQ
